

INTERCOLLEGIATE ATHLETICS BASKETBALL TRAINING FACILITY

PROJECT CONTACTS

Bob Dillon

Construction Project Manager

Project Delivery Group

bdillon@uw.edu | 206.423.5155

UNIVERSITY of WASHINGTON

Sydney Thiel *Project Manager* Project Delivery Group sydthiel@uw.edu | 206.960.2417

UNIVERSITY of WASHINGTON

ABOUT THE PROJECT

- 36,000 sf (new facility) + 4,000 sf (interior renovation)
 = 40,000 sf total project
- 2 stories in height (approximately 40')
- Supports Men's and Women's Basketball programs
- Direct Connections to Hec Ed and Graves Annex for all athletes



CLICK OR SCAN TO LEARN MORE

SUMMARY OF UPCOMING ACTIVITIES (April 15 - May 30, 2024)

The project is continuing with the installation of underground utilities and finishing up the abatement removal inside the Pavilion Pool building. As this works progresses, you can expect to see vac-trucks and excavators being used within the site as the utilities are being installed. Additionally, the band room remodel is starting up and the project team is getting ready for the start of the Pavilion Pool building demo, which happens at the end of May.

IMPACT BULLETIN

IMPACT TYPE	INFORMATION	IMPACT DATES
NOISE	 Graves Annex Steam Pipe Re-route Hec Ed Steam Tunnel Band Room Remodel Vac trucking for Utilities Demo of Pool Pavilion 	 Mar 18 - May 30 Mar 8 - June 6 Apr 08- Aug 1 Mar 18 - May 30 May 31 - July 5
ODOR	Switchover of gas line	• Apr 15 - Apr 19
CLOSURES/ TRANSPORT	 Pedestrian walk/bike path re-routed by Nordstrom Power Line Switchover Steam Line Switchover 	 Mar 1 - Aug 2025 May 13 - May 17 May 18 - May 20


UPCOMING MILESTONES

1			Н			
APRIL 2024						
	-1	2	3	4	5	6
7	8	9	10	-11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

- Apr 8-19: Band Room move-out
- Apr 22: Band Room Remodel Starts
- Apr 18: Gas Line Switchover



- May 13-17 Power Line Switchover
- May 18-20: Steam Line Switchover
- May 31: Start of Pool Pavilion Demo

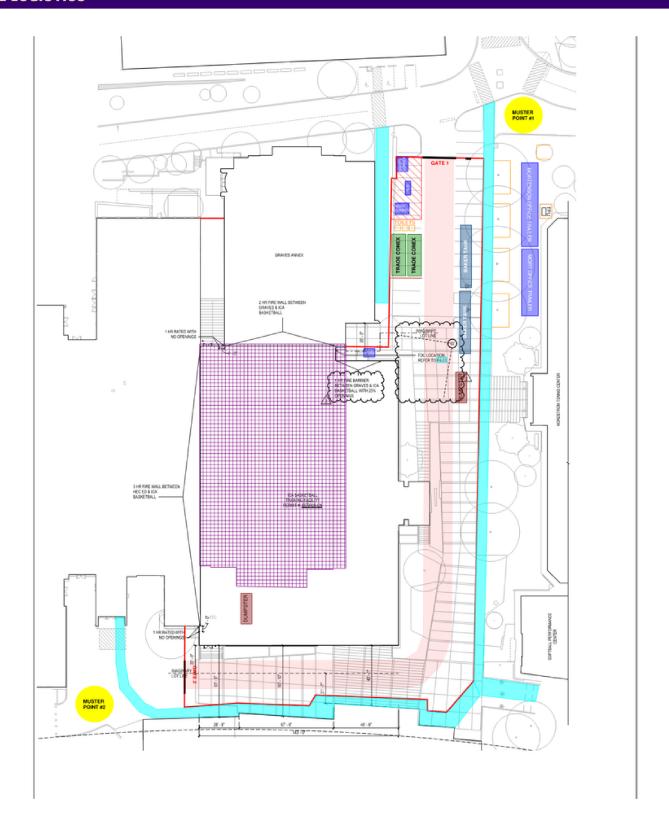

Site Logistics Legend

