



INTERCOLLEGIATE ATHLETICS BASKETBALL TRAINING FACILITY

PROJECT CONTACTS

Sydney Thiel
Project Manager
 Project Delivery Group
 sydthiel@uw.edu | 206.960.2417

UNIVERSITY of
 WASHINGTON

Bob Dillon
Construction Project Manager
 Project Delivery Group
 bdillon@uw.edu | 206.423.5155

UNIVERSITY of
 WASHINGTON

ABOUT THE PROJECT

- 36,000 sf (new facility) + 4,000 sf (interior renovation) = 40,000 sf total project
- 2 stories in height (approximately 40')
- Supports Men's and Women's Basketball programs
- Direct Connections to Hec Ed and Graves Annex for all athletes



CLICK OR SCAN TO LEARN MORE


SUMMARY OF UPCOMING ACTIVITIES (June 15 - July 30, 2024)

The project is continuing with the underground utility install while also starting the main building demo this month. You will continue to see vac-trucks and excavators for the utility work in addition to larger pieces of equipment for the building demo. When demo is completed in mid/late July, soldier pile installation will commence along the west and south elevations of the job site. You can expect to hear loud drilling during the demo and soldier pile install activities. Drywall and interior finishes work is also progressing in the Graves Annex and Hec Ed spaces, with turnover of those spaces expected during the month of July.


IMPACT BULLETIN

IMPACT TYPE	INFORMATION	IMPACT DATES
NOISE	<ul style="list-style-type: none"> • Graves Annex Temp Wall Removed • Hec Ed Band Room Remodel • Utility Installation • Pool Pavilion Demo 	<ul style="list-style-type: none"> • July 12 • Apr 8- July 31 • Mar 18 - Aug 07 • June 24 - July 24
MINOR VIBRATION	<ul style="list-style-type: none"> • Sheet Piling Install for Storm Utility • Pool Pavilion Demo • Soldier Pile Drilling 	<ul style="list-style-type: none"> • May 15 - June 21 • June 24 - July 24 • July 30 - Aug 10
CLOSURES/ TRANSPORT	<ul style="list-style-type: none"> • Pedestrian walk/bike path re-routed by Nordstrom • Hec Ed Break Room & Security Office (intermittently) 	<ul style="list-style-type: none"> • Mar 1 - Aug 2025 • June 24 - July 24


UPCOMING MILESTONES



- *June 24: Structural Demo of Pool Pavilion Starts*



- *July 12: Graves Annex Work Complete*
- *July 30: Install Soldier Piles*
- *July 31: Hec Ed Band Room Complete*

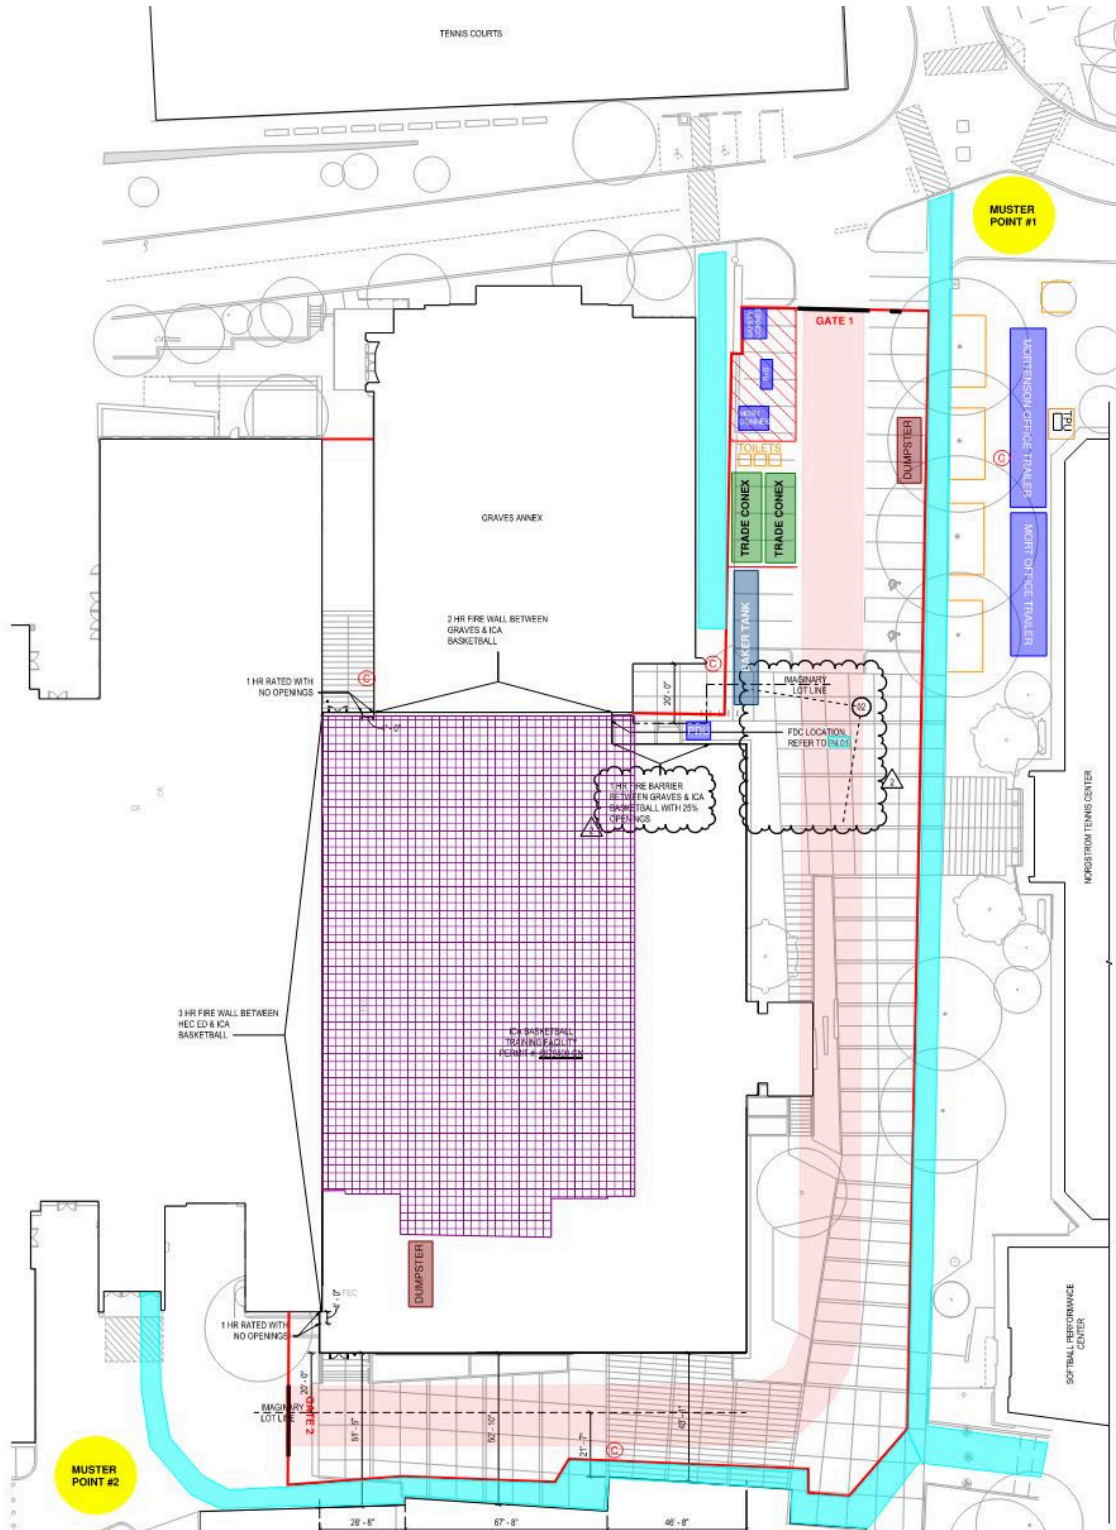

Site Logistics Legend

- Existing Building Footprint
- Pedestrian Walk Path
- Bike Path
- Site Fence
- Office Trailers
