

INTERCOLLEGIATE ATHLETICS BASKETBALL TRAINING FACILITY

PROJECT CONTACTS

Carmen Scraper

Project Manager

Project Delivery Group

cscraper@uw.edu | 206.833.6989

Bob Dillon Construction Project Manager Project Delivery Group bdillon@uw.edu | 206.423.5155

UNIVERSITY of WASHINGTON

ABOUT THE PROJECT

- 36,000 sf (new facility) + 4,000 sf (interior renovation)
 = 40,000 sf total project
- 2 stories in height (approximately 40')
- · Supports Men's and Women's Basketball programs
- Direct Connections to Hec Ed and Graves Annex for all athletes



CLICK OR SCAN TO LEARN MORE

SUMMARY OF UPCOMING ACTIVITIES (December 15 - January 31, 2024)

The project has finished its underground foundation and shotcrete work and is getting prepped for slab on grade placements. Throughout the next month, the underground electrical, plumbing, and foundation drainage will be completed. Once that is done, the slab on grade will be placed and the base of the construction site will be covered with concrete instead of mud. You will continue to see concrete trucks throughout the month and when slab on grade placement is finished that will change to a crane as steel erection begins.

IMPACT BULLETIN

IMPACT TYPE	INFORMATION	IMPACT DATES		
NOISE	Bolt Rattling/Tightening for Steel	• January 24 - March 18		
FLASH AWARENESS	Welding (Steel)	• January 24 - March 18		
CLOSURES/ TRANSPORT	 Pedestrian walk/bike path re- routed by Nordstrom South Side of Graves Roof 	Mar 1 - Aug 2025January 24 - March 18		


UPCOMING MILESTONES

0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0								
SUN	MON	TUE	WED	THU	FRI	SAT		
1	2	3	4	5	6	7		
8	9	10	-11	12	13	14		
15	16	17	18	19	20	21		
22	23	24	25	26	27	28		
29	30	31						

- December 13: Slab on Grade Activities Start
- December 20: Court-A Slab on Grade Placement



- January 6: Court-B Slab on Grade Placement
- January 24: Steel Erection Begins

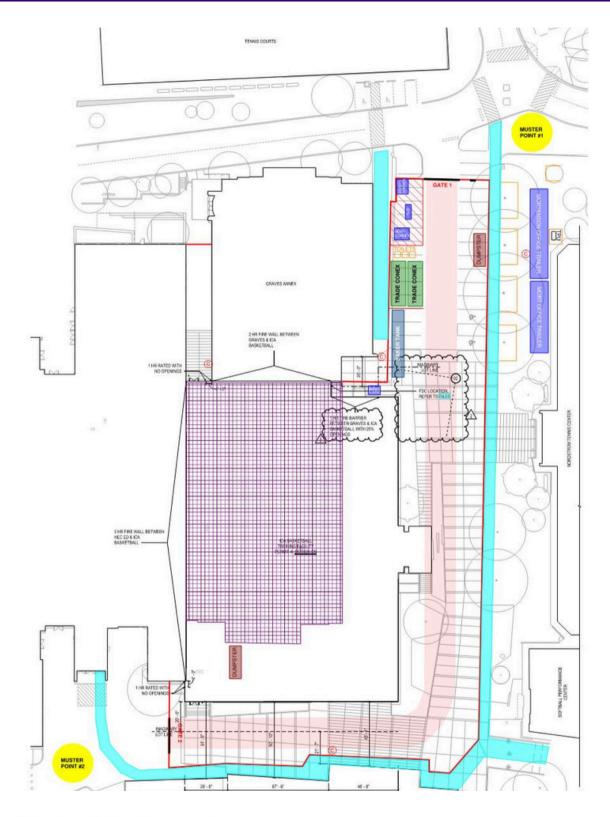

Site Logistics Legend

