



INTERCOLLEGIATE ATHLETICS BASKETBALL TRAINING FACILITY

PROJECT CONTACTS

Carmen Scrapper
Project Manager
 Project Delivery Group
 cscraper@uw.edu | 206.833.6989



Bob Dillon
Construction Project Manager
 Project Delivery Group
 bdillon@uw.edu | 206.423.5155



ABOUT THE PROJECT

- 36,000 sf (new facility) + 4,000 sf (interior renovation) = 40,000 sf total project
- 2 stories in height (approximately 40')
- Supports Men's and Women's Basketball programs
- Direct Connections to Hec Ed and Graves Annex for all athletes



[CLICK OR SCAN TO LEARN MORE](#)

SUMMARY OF UPCOMING ACTIVITIES (January 15 - February 28, 2024)

The project is finishing up its slab on grade placements and is gearing up to start steel erection at the end of January. You will continue to see concrete trucks on site during this month. At the end of January, the concrete trucks will be replaced with a 155 ton crane, which will be used for steel erection. The progress of construction is starting to move upwards, and in the beginning of February you will quickly see the frame of the building built out. This work requires a lot of bolting and welding so expect to see sparks and hear drilling noises throughout the month of February.


IMPACT BULLETIN

IMPACT TYPE	INFORMATION	IMPACT DATES
NOISE	<ul style="list-style-type: none"> • Bolt Rattling/Tightening for Steel 	<ul style="list-style-type: none"> • January 24 - March 18
FLASH AWARENESS	<ul style="list-style-type: none"> • Welding (Steel) 	<ul style="list-style-type: none"> • January 24 - March 18
CLOSURES/ TRANSPORT	<ul style="list-style-type: none"> • Pedestrian walk/bike path re-routed by Nordstrom • South Side of Graves Roof 	<ul style="list-style-type: none"> • Mar 1 - Aug 2025 • January 24 - March 18


UPCOMING MILESTONES








- *January 24: Steel Erection Begins*

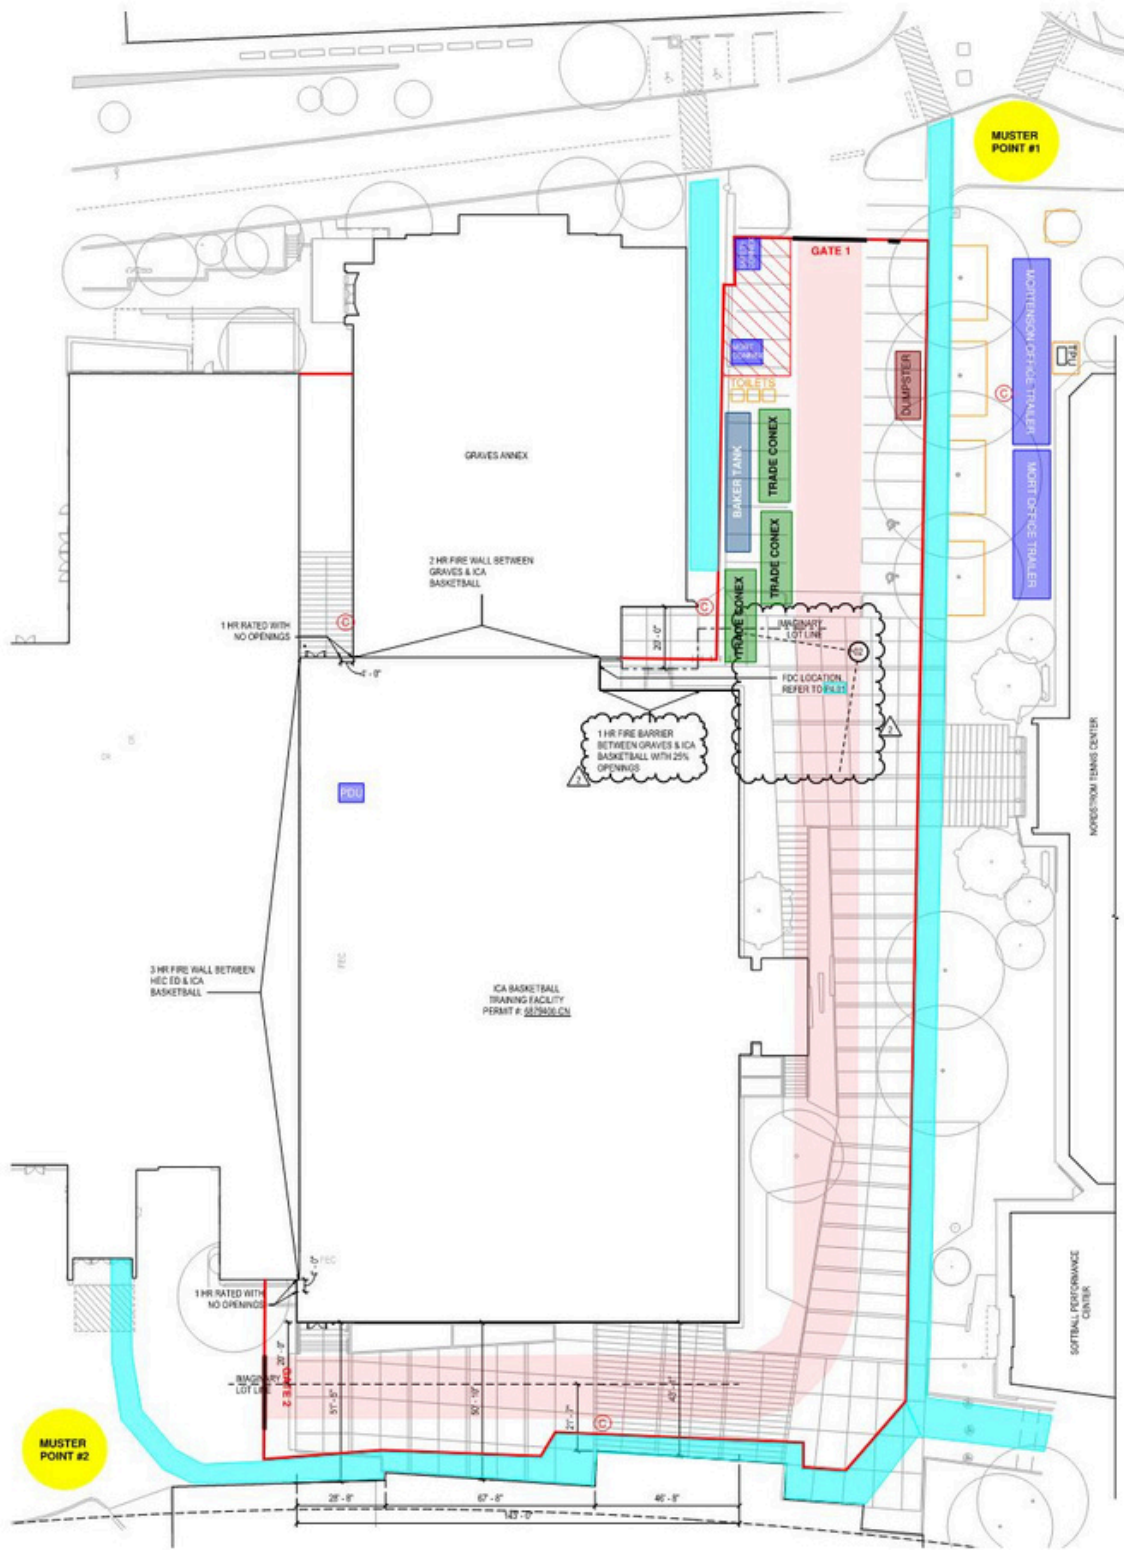

- *February 4: Steel Joist Install Starts*
- *February 17: Metal Decking Install Starts*



Site Logistics Legend

-  Existing Building Footprint
-  Pedestrian Walk Path
-  Fire Lane
-  Site Fence
-  Office Trailers
