



INTERCOLLEGIATE ATHLETICS BASKETBALL TRAINING FACILITY

PROJECT CONTACTS

Carmen Scrapper
Project Manager
 Project Delivery Group
 cscraper@uw.edu | 206.833.6989



Bob Dillon
Construction Project Manager
 Project Delivery Group
 bdillon@uw.edu | 206.423.5155



ABOUT THE PROJECT

- 36,000 sf (new facility) + 4,000 sf (interior renovation) = 40,000 sf total project
- 2 stories in height (approximately 40')
- Supports Men's and Women's Basketball programs
- Direct Connections to Hec Ed and Graves Annex for all athletes



CLICK OR SCAN TO LEARN MORE


SUMMARY OF UPCOMING ACTIVITIES (March 15 - April 30, 2025)

The structural steel and main building concrete work is complete and the project is fully in the enclosure phase of work. You will notice that the building façade is starting to take shape, with the metal framing continuing and then the installation of the metal panels, polycarbonate panels, and brick. While this work is progressing, the roof will be installed and the building will be fully enclosed. While the enclosure work is happening on the outside of the building, the mechanical, electrical, and plumbing trades are working on the inside of the building. All of this work is coming together for the start of interior finishes which will occur in May.


IMPACT BULLETIN

IMPACT TYPE	INFORMATION	IMPACT DATES
NOISE	<ul style="list-style-type: none"> • Bolting/Anchoring for Enclosure Systems 	<ul style="list-style-type: none"> • February 25 - April 16
FLASH AWARENESS	<ul style="list-style-type: none"> • Welding (Enclosure) 	<ul style="list-style-type: none"> • February 25 - April 16
CLOSURES/ TRANSPORT	<ul style="list-style-type: none"> • Pedestrian walk/bike path re-routed by Nordstrom • South Side of Graves Roof 	<ul style="list-style-type: none"> • Mar 1 2024 - Aug 2025 • January 24 - March 04

UPCOMING MILESTONES




- *March 17: Insulated Metal Panels Starts*
- *March 31: Polycarbonate Panel Install Starts*









- *April 10: Mechanical equipment on Roof Start*

COURT A RENDERING

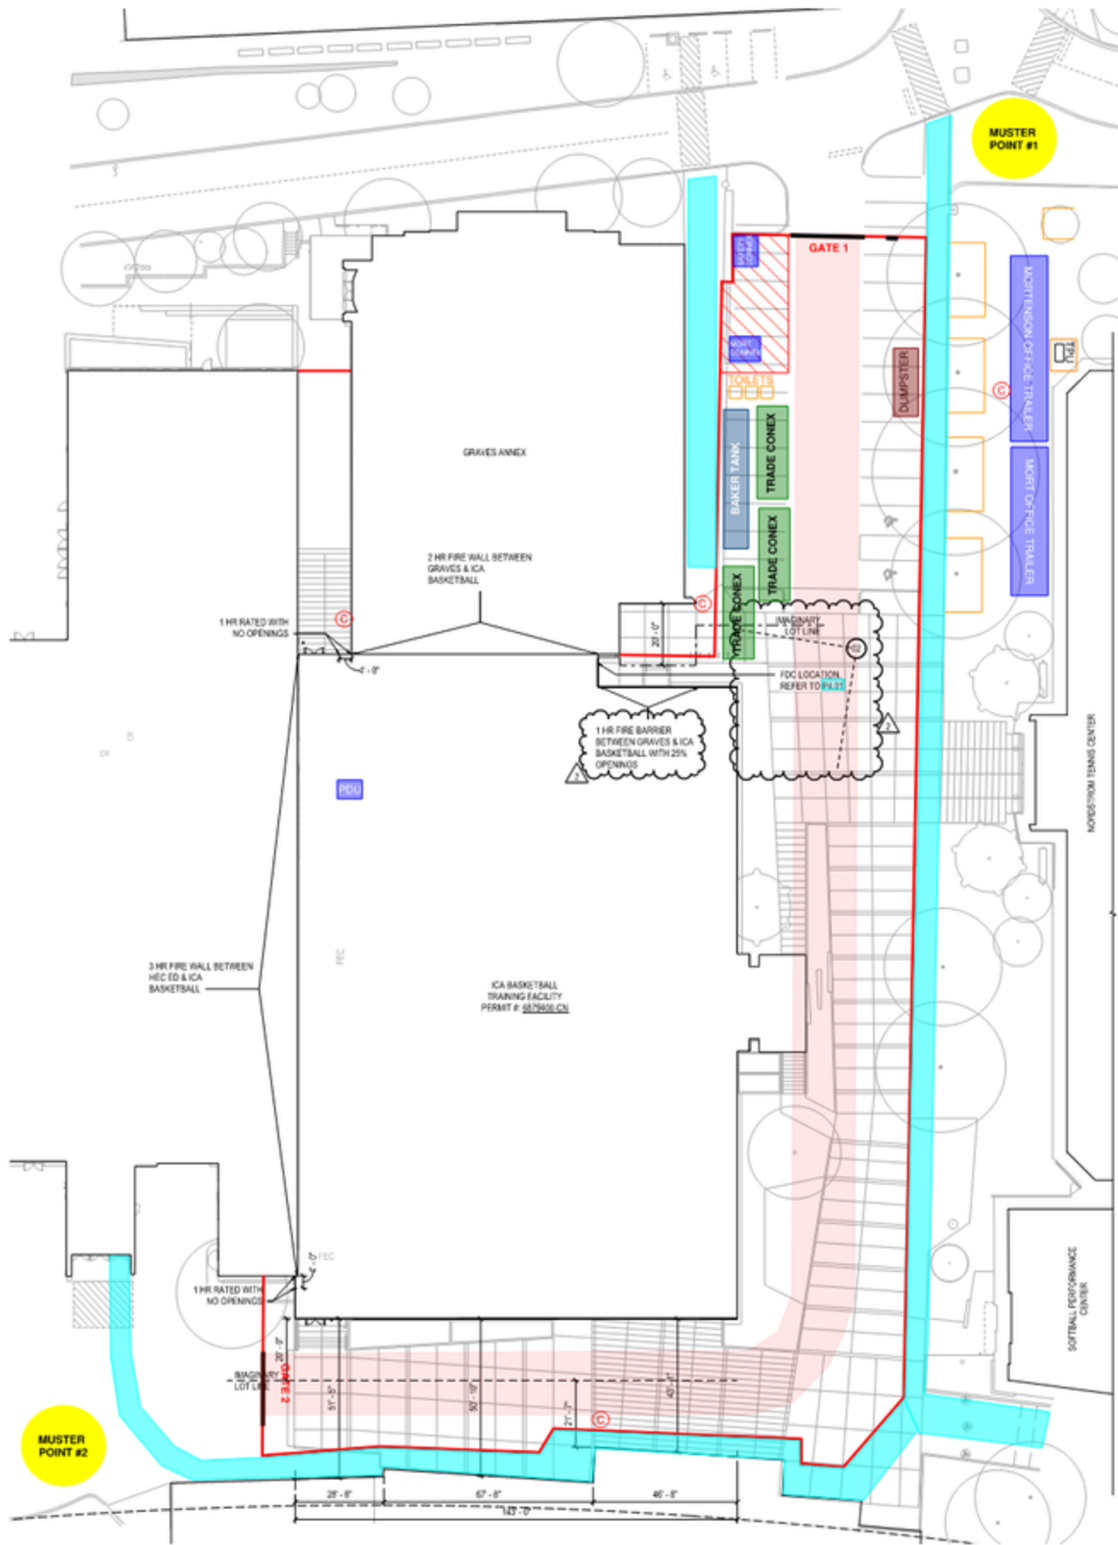



Site Logistics Legend

-  Existing Building Footprint
-  Pedestrian Walk Path
-  Bike Path
-  Site Fence
-  Fire Lane
-  Office Trailers
